


Mitsue Project

Phases & Funding Flowchart



Version	v2.6
Date	2026-07-03
Author	Rob Oudendijk

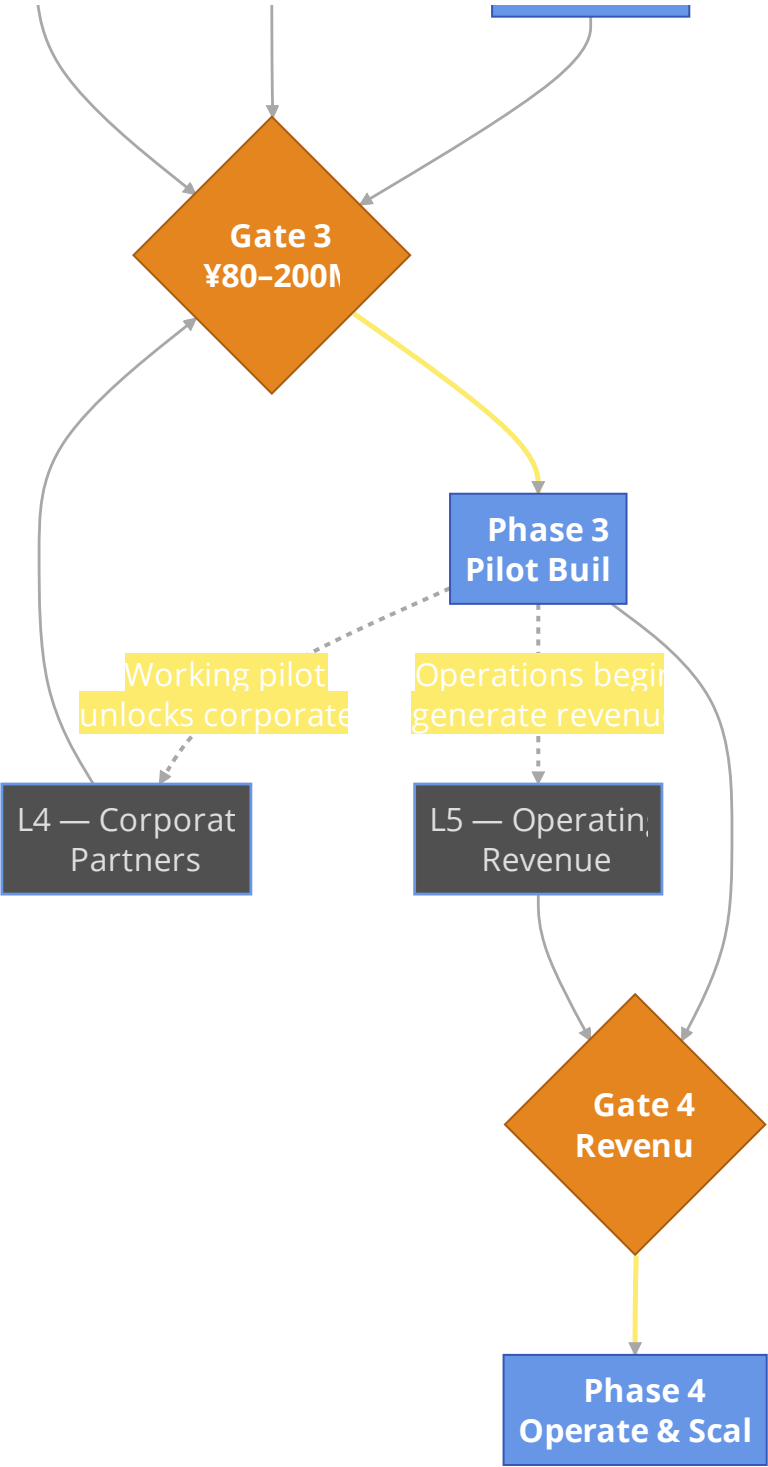

Legend

Shape / Colour	Meaning
Light-blue box (#6796e6)	Project phase — what gets done
Orange diamond (#e58520)	Funding gate — checkpoint between phases
Slate box, light-blue border (#505050 / #6796e6)	Funding source / layer
Dark dashed box, yellow border	Hold or descope action when a gate fails
Solid arrow	Sequential flow / funding inflow
Dotted arrow	Feedback loop — phase deliverables unlock the next funding layer

How to read it

1. Read the top row left-to-right — that is the project's forward path through the five phases.

- 2. **Yellow diamonds are decision gates.** Each one asks: "Have we secured enough funding to begin the next phase?" If yes → proceed; if short → loop into a grey hold/descope box and re-pitch.
- 3. **The bottom row is the funding stack.** Arrows go *upward* into the gate that each funding source unlocks.
- 4. **Dotted arrows close the loop.** Completing a phase produces deliverables (feasibility studies, legal entity, working pilot) that themselves *unlock the next layer* of funding. This is the engine of the project.

Funding Stack — Current Position (Baseline Rev 1, May 2026)

Funding Layer	Source	Amount (¥M)
L1 — Founders	Founder capital (Rob Oudendijk)	¥6M
L2 — Government Grants	National + prefectural + municipal grants	¥115M
L3 — Foundations	Philanthropic foundations	¥33M
L4 — Corporate Partners	Corporate sustainability / CSR	¥35M
L5 — Operating Revenue	Early data center, biomass/solar energy, and EV revenue	¥3M
Total Raised / Committed		¥192M
BAC (PMB)	Project budget baseline	¥220M
Management Reserve	Board-controlled reserve	¥25M
Total Project Budget		¥245M
Funding Gap vs BAC	Additional funding required to meet BAC	¥28M
Funding Gap vs Total Budget	Additional funding required including MR	¥53M

Note: The ¥28M–¥53M funding gap is to be closed through additional government grants, new corporate partnerships, or bridge financing secured during Phase 2 (M10–M18). The funding stack above reflects commitments and realistic pipeline as of May 2026 — it is not a target to be artificially inflated. The gap is shown explicitly because stakeholders deserve an honest picture. **A named, concrete path to closing a meaningful part of this gap is the village-led 地域脱炭素移行・再エネ推進交付金 (MoE, step 2 of the national decarbonization funding ladder): 2/3–3/4 subsidy on solar/battery/EV/private-wire capex, paid to the village via official 官民連携, targeting Phases 2–3.** L2 (Government grants) in Diagram 2 now includes this route routed through the municipality. Baseline Rev 2 (due M9, Dec 2026) should fold in any confirmed 交付金 amount.

Sources: MoE — 地域脱炭素移行・再エネ推進交付金: <https://policies.env.go.jp/policy/roadmap/grants/> · 実施要領 (補助率 2/3・3/4 条件) : <https://www.env.go.jp/content/900470616.pdf>

Derived from `mitsue_implementation_plan.md` — May 2026
