

Mitsue Project — Phases & Funding Flowchart

Diagram 1 — Phase Spine with Funding Gates






Diagram 2 — Funding Sources Feeding Each Gate

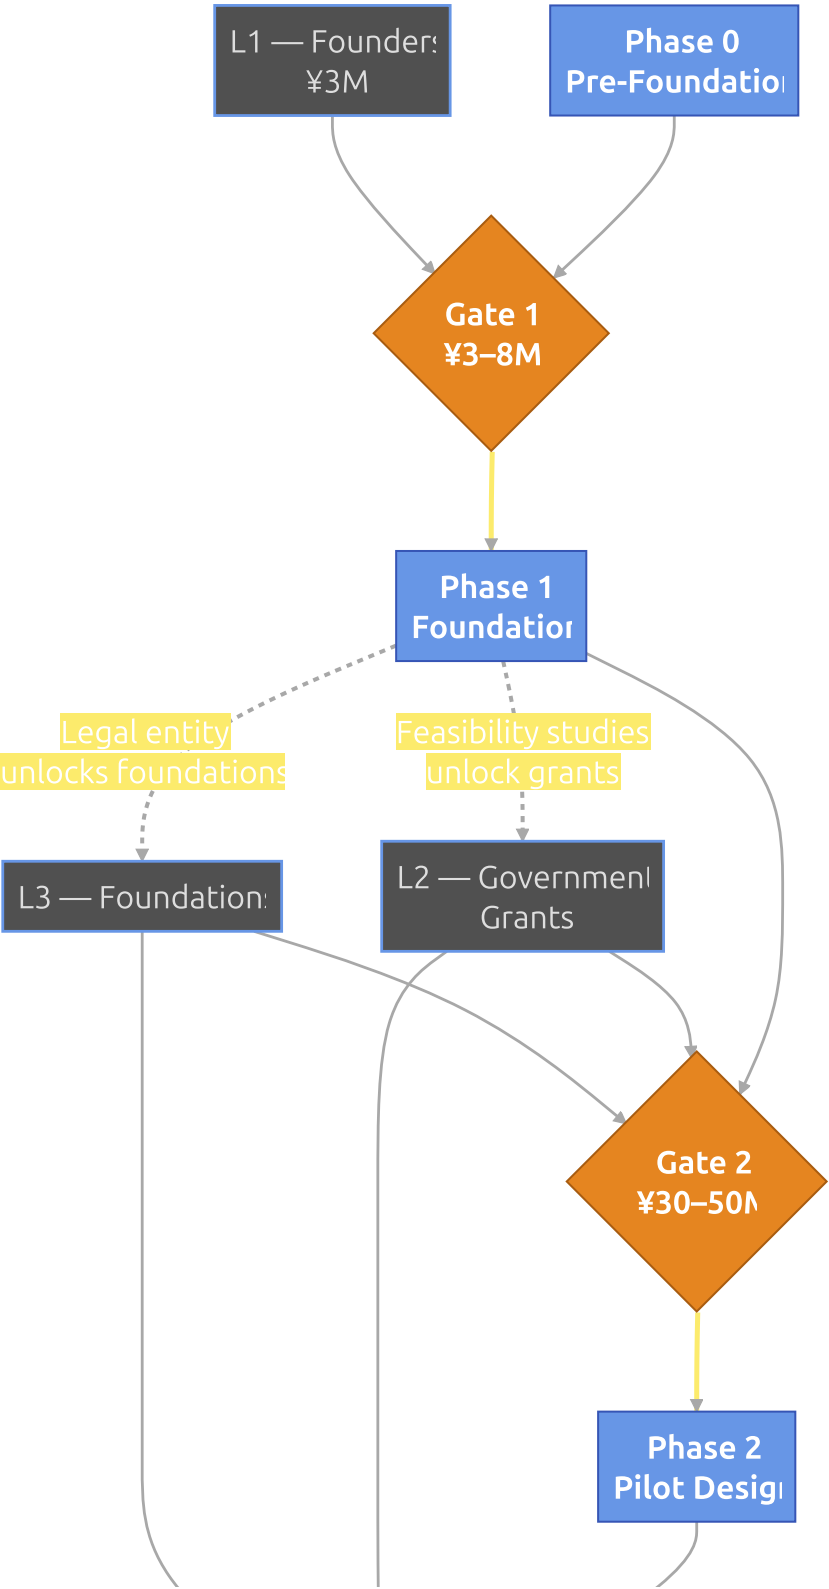

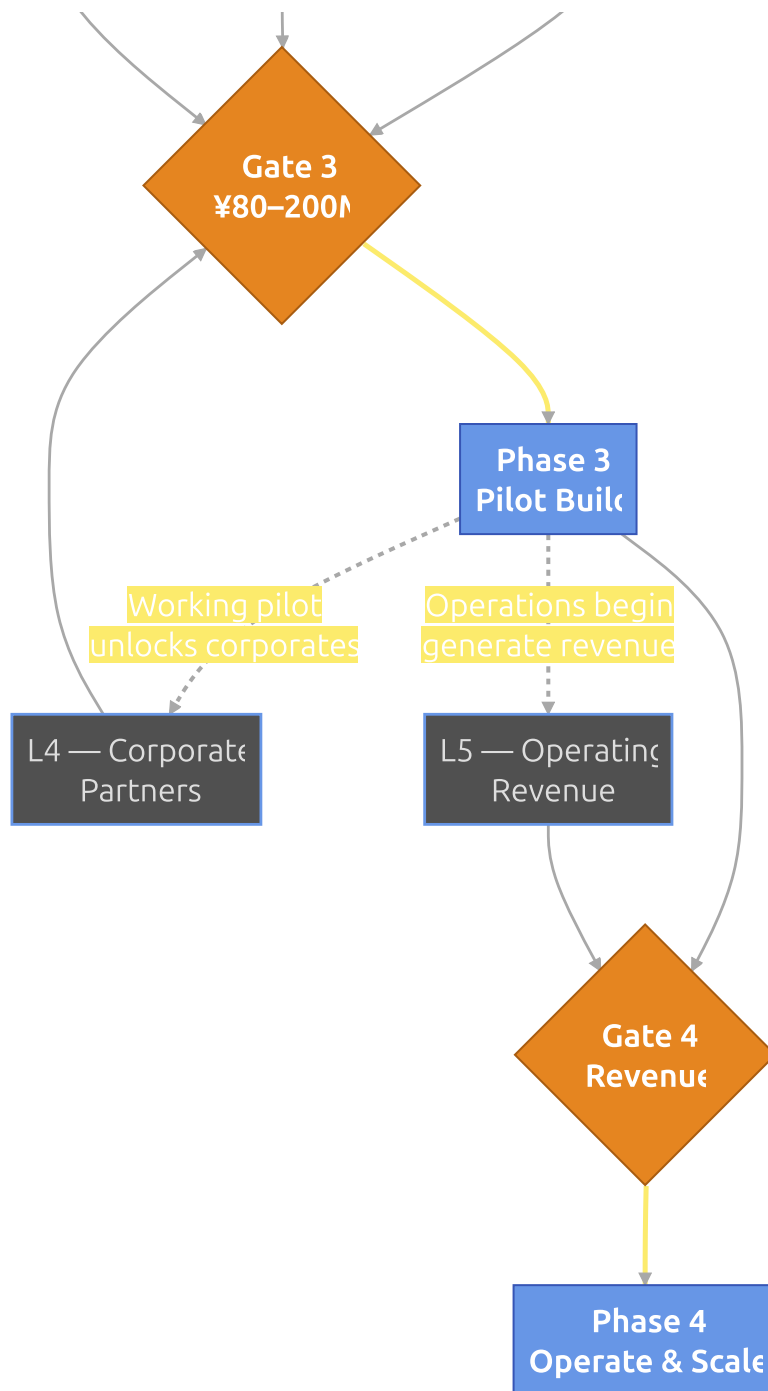

Legend

Shape / Colour	Meaning
Light-blue box (#6796e6)	Project phase — what gets done
Orange diamond (#e58520)	Funding gate — checkpoint between phases
Slate box, light-blue border (#505050 / #6796e6)	Funding source / layer
Dark dashed box, yellow border	Hold or descope action when a gate fails
Solid arrow	Sequential flow / funding inflow
Dotted arrow	Feedback loop — phase deliverables unlock the next funding layer

How to read it

1. **Read the top row left-to-right** — that is the project's forward path through the five phases.

2. **Yellow diamonds are decision gates.** Each one asks: *"Have we secured enough funding to begin the next phase?"* If yes → proceed; if short → loop into a grey hold/descope box and re-pitch.
3. **The bottom row is the funding stack.** Arrows go *upward* into the gate that each funding source unlocks.
4. **Dotted arrows close the loop.** Completing a phase produces deliverables (feasibility studies, legal entity, working pilot) that themselves *unlock the next layer* of funding. This is the engine of the project.

Funding Stack — Current Position (Baseline Rev 1, May 2026)

Funding Layer	Source	Amount (¥M)
L1 — Founders	Founder capital (Rob Oudendijk)	¥6M
L2 — Government Grants	National + prefectural + municipal grants	¥115M
L3 — Foundations	Philanthropic foundations	¥33M
L4 — Corporate Partners	Corporate sustainability / CSR	¥35M
L5 — Operating Revenue	Early data center, biomass/solar energy, and EV revenue	¥3M
Total Raised / Committed		¥192M
BAC (PMB)	Project budget baseline	¥220M
Management Reserve	Board-controlled reserve	¥25M
Total Project Budget		¥245M
Funding Gap vs BAC	Additional funding required to meet BAC	¥28M
Funding Gap vs Total Budget	Additional funding required including MR	¥53M

Note: The ¥28M–¥53M funding gap is to be closed through additional government grants, new corporate partnerships, or bridge financing secured during Phase 2 (M10–M18). The funding stack above reflects commitments and realistic pipeline as of May 2026 — it is not a target to be artificially inflated. The gap is shown explicitly because stakeholders deserve an honest picture.

Derived from [mitsue_implementation_plan.md](#) — May 2026
