Mitsue ai data center

OpenProject

All open

Create | Include projects

ID	TYPE	SUBJECT	STATUS	START DATE	FINISH DATE	DURATION
123	TASK	[Risk] Founder dependency on Rob	In progress	04/01/2026	12/31/2026	197 days
122	TASK	[Risk] Funding gaps between phases	In progress	04/01/2026	12/31/2030	1240 days
38	SUMMARY TASK	Phase 0	New	04/01/2026	10/02/2026	185 days
48	TASK	Open project Slack/Signal/email list	In progress	05/11/2026	06/23/2026	32 days
46	TASK	Confirm support letter intent — Sandra Pellegrom / Dutch C...	In progress	05/11/2026	06/17/2026	28 days
39	TASK	Private meeting with Mitsue village mayor	In progress	05/16/2026	05/30/2026	15 days
40	TASK	Meet 自治会 leaders in Sugano + surrounding hamlets	New	05/19/2026	06/01/2026	10 days
47	TASK	Reach out to 1–2 candidate 行政書士 in Nara	New	06/01/2026	07/08/2026	28 days
43	TASK	Quiet conversations with 2–3 sympathetic landowners	New	06/01/2026	06/10/2026	8 days
41	TASK	Identify and confirm Japanese co-founder	In progress	06/01/2026	07/31/2026	45 days
42	TASK	Identify 3–5 founding team members	In progress	08/03/2026	10/02/2026	45 days
127	TASK	[Risk] Team conflict / mission drift	In progress	07/01/2026	12/31/2030	1175 days
125	TASK	[Risk] Fiber connectivity insufficient	In progress	07/01/2026	12/31/2026	132 days
124	TASK	[Risk] Building unsuitable for data center	In progress	07/01/2026	12/31/2026	132 days
121	TASK	[Risk] Forestry economics worse than expected	In progress	07/01/2026	12/31/2026	132 days
115	SUMMARY TASK	[Legal] Pro support	New	07/01/2026	12/31/2027	393 days
118	TASK	弁護士 consult — landowner contracts	New	07/01/2026	03/31/2027	196 days
117	TASK	Engage 公認会計士 / 税理士	New	07/01/2026	09/30/2026	66 days
116	TASK	Engage 行政書士 (Nara-based ideal)	New	07/09/2026	09/08/2026	44 days
119	TASK	Patent attorney — only if novel IP arises	New	01/01/2027	12/31/2027	261 days
100	SUMMARY TASK	[Legal] Entity & Tax	New	07/01/2026	03/31/2027	196 days
101	TASK	一般社団法人 incorporation	New	07/01/2026	09/01/2026	45 days
104	TASK	Accounting system (e.g. 弥生会計)	New	09/01/2026	11/02/2026	45 days
103	TASK	Bank account opening	New	09/01/2026	09/30/2026	22 days
102	TASK	Tax registration (法人税, 消費税)	New	09/01/2026	09/30/2026	22 days

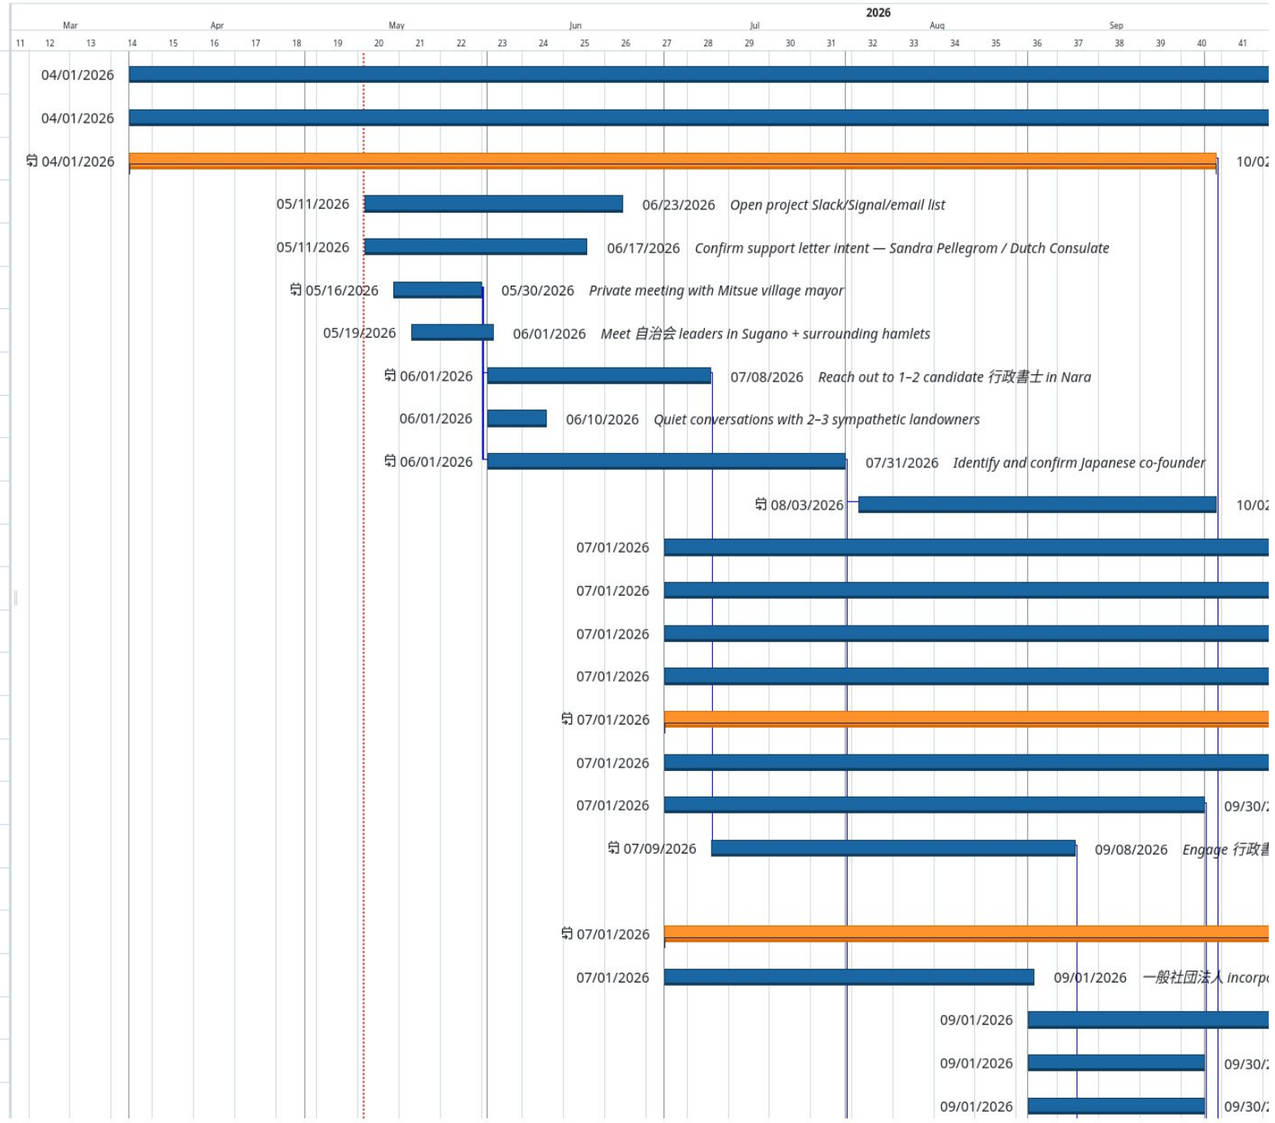

Mitsue ai data center

OpenProject

Search in OpenProject

All open

Create | Include projects 1 | Baseline | Filt

ID	TYPE	SUBJECT	STATUS	START DATE
49	SUMMARY TASK	Phase 1	New	10/05/2026
59	TASK	Commission Connectivity Assessment	New	10/05/2026
58	TASK	Commission Building & Site Assessment	New	10/05/2026
57	TASK	Commission Energy Systems Feasibility Study	New	10/05/2026
56	TASK	Commission Forestry Feasibility Study	New	10/05/2026
50	TASK	Draft 定款 (articles of incorporation)	New	10/05/2026
51	TASK	Notarize 定款	New	11/05/2026
52	TASK	Register 一般社団法人 with Legal Affairs Bureau	New	12/09/2026
62	TASK	Formalize advisory board	New	01/08/2027
61	TASK	Launch bilingual project website (basic, professional)	New	01/08/2027
60	TASK	Secure letter of interest from Mitsue village government	New	01/08/2027
54	TASK	Open corporate bank account	New	01/08/2027
53	TASK	Tax registration (法人税, 消費税)	New	01/08/2027
55	TASK	Set up accounting system (e.g. 弥生会計)	New	02/09/2027
126	TASK	[Risk] Regulatory delays	New	01/01/2027
106	SUMMARY TASK	[Legal] Permits	New	01/01/2027
113	TASK	Environmental impact — 環境アセスメント (if scale triggers)	New	01/01/2027
109	TASK	Building conversion — 建築基準法	New	01/01/2027
108	TASK	Land use coordination — 農業委員会 if agricultural land	New	01/01/2027
107	TASK	Forestry permit — 伐採届出 (Forest Act)	New	01/01/2027
111	TASK	Electrical — 電気事業法 compliance	New	02/01/2027
110	TASK	Fire & safety — 消防 approvals for biomass	New	02/01/2027
112	TASK	FIT/FIP registration — METI	New	03/01/2027
114	TASK	Data center compliance — APPI + cybersecurity	New	06/01/2027
