



# Mitsue Project — Phases & Funding Flowchart


Diagram 1 — Phase Spine with Funding Gates



# Diagram 2 — Funding Sources Feeding Each Gate

---

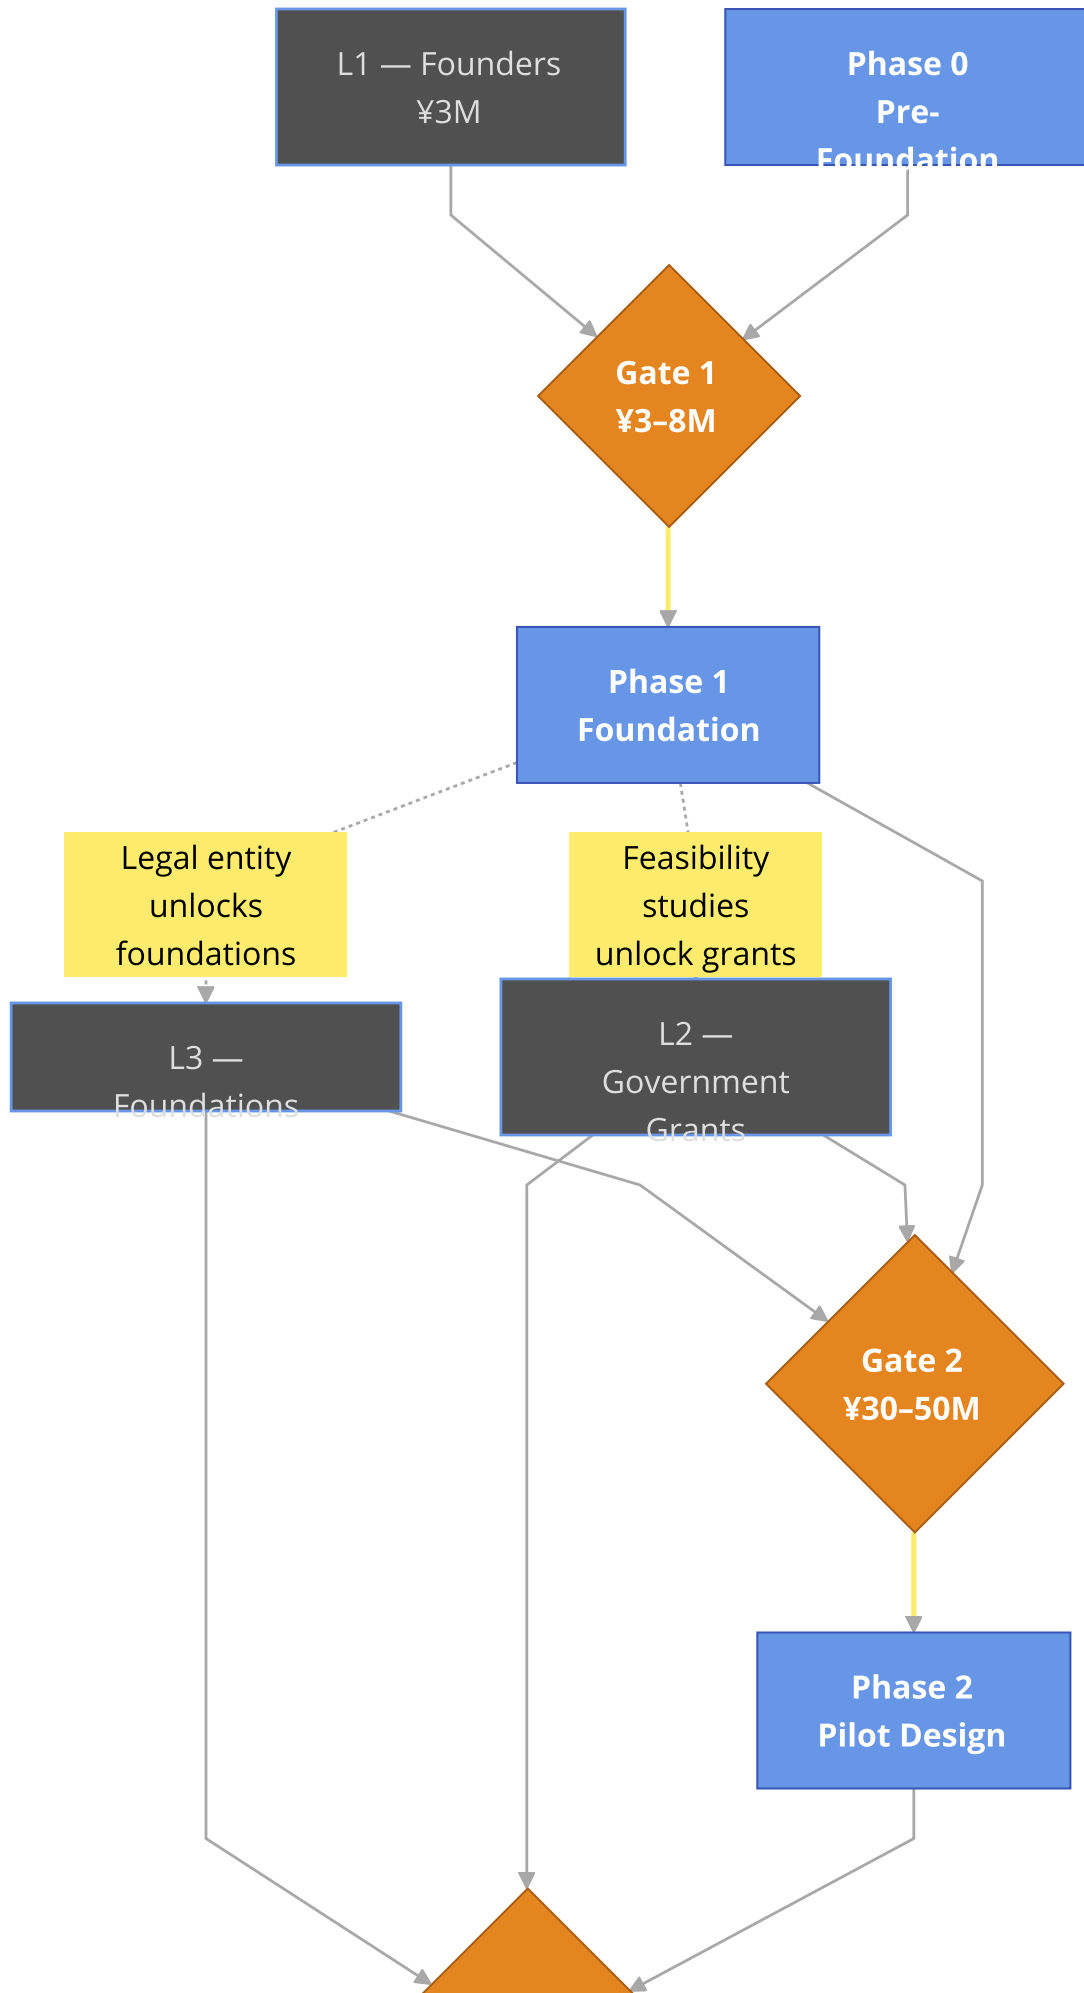

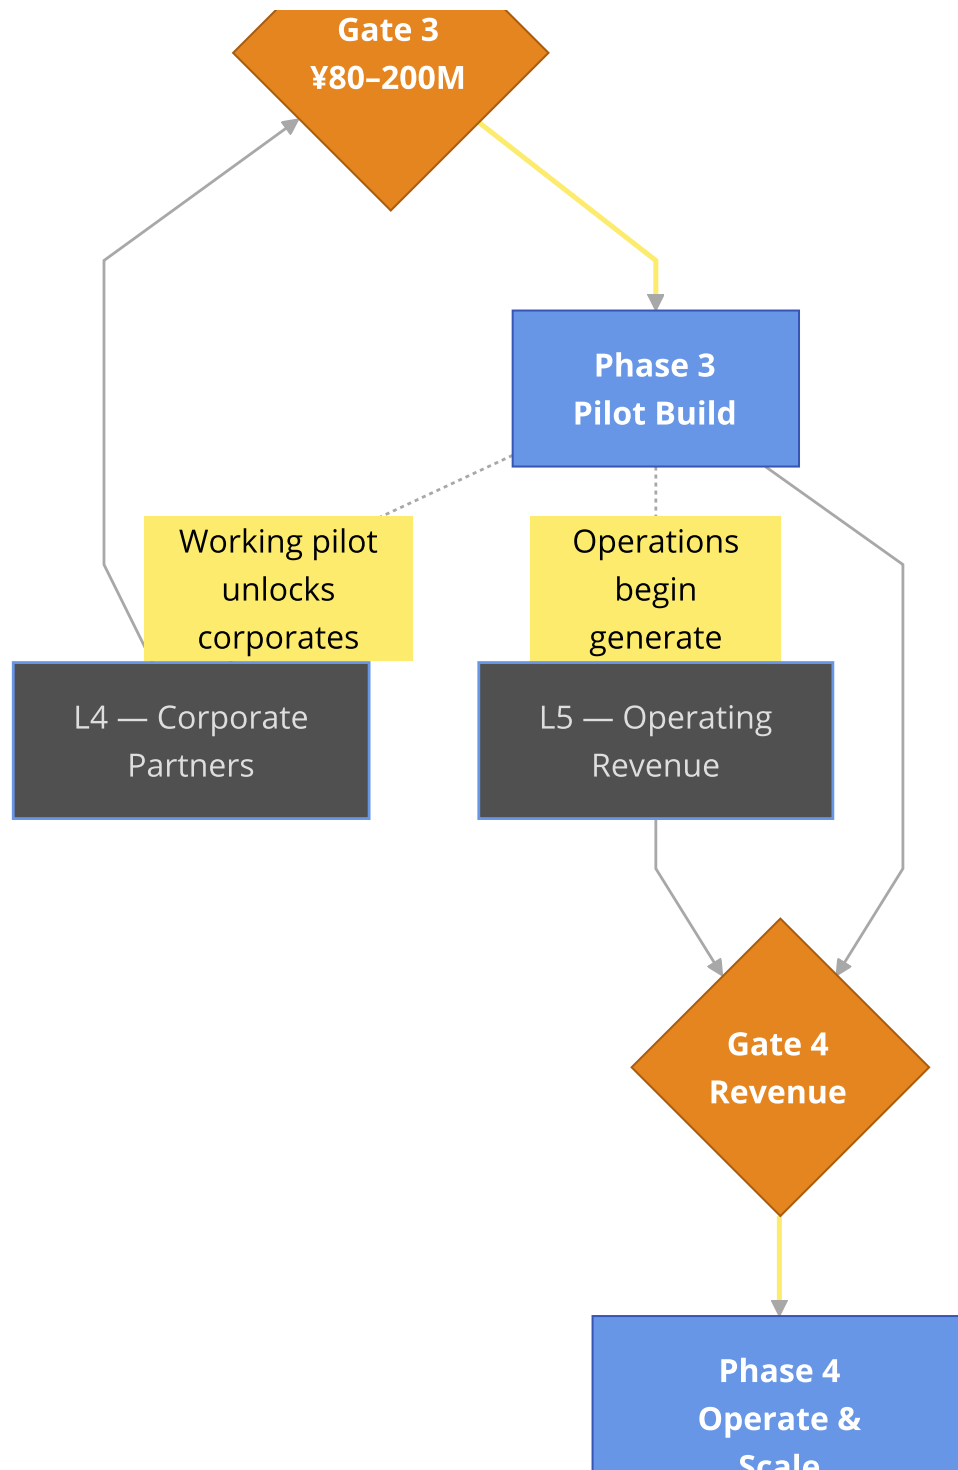

## Legend

| Shape / Colour                                            | Meaning                                  |
|-----------------------------------------------------------|------------------------------------------|
| <b>Light-blue box</b> ( #6796e6 )                         | Project phase — what gets done           |
| <b>Orange diamond</b> ( #e58520 )                         | Funding gate — checkpoint between phases |
| <b>Slate box, light-blue border</b> ( #505050 / #6796e6 ) | Funding source / layer                   |

| Shape / Colour                 | Meaning                                                          |
|--------------------------------|------------------------------------------------------------------|
| Dark dashed box, yellow border | Hold or descope action when a gate fails                         |
| Solid arrow                    | Sequential flow / funding inflow                                 |
| Dotted arrow                   | Feedback loop — phase deliverables unlock the next funding layer |

## How to read it

1. **Read the top row left-to-right** — that is the project's forward path through the five phases.
2. **Yellow diamonds are decision gates.** Each one asks: *"Have we secured enough funding to begin the next phase?"* If yes → proceed; if short → loop into a grey hold/descope box and re-pitch.
3. **The bottom row is the funding stack.** Arrows go *upward* into the gate that each funding source unlocks.
4. **Dotted arrows close the loop.** Completing a phase produces deliverables (feasibility studies, legal entity, working pilot) that themselves *unlock the next layer* of funding. This is the engine of the project.

## Funding Stack — Current Position (Baseline Rev 1, May 2026)

| Funding Layer                      | Source                                    | Amount (¥M)  |
|------------------------------------|-------------------------------------------|--------------|
| L1 — Founders                      | Founder capital (Rob Oudendijk)           | ¥6M          |
| L2 — Government Grants             | National + prefectural + municipal grants | ¥115M        |
| L3 — Foundations                   | Philanthropic foundations                 | ¥33M         |
| L4 — Corporate Partners            | Corporate sustainability / CSR            | ¥35M         |
| L5 — Operating Revenue             | Early data center and EV revenue          | ¥3M          |
| <b>Total Raised / Committed</b>    |                                           | <b>¥192M</b> |
|                                    |                                           |              |
| <b>BAC (PMB)</b>                   | Project budget baseline                   | <b>¥220M</b> |
| <b>Management Reserve</b>          | Board-controlled reserve                  | ¥25M         |
| <b>Total Project Budget</b>        |                                           | <b>¥245M</b> |
|                                    |                                           |              |
| <b>Funding Gap vs BAC</b>          | Additional funding required to meet BAC   | <b>¥28M</b>  |
| <b>Funding Gap vs Total Budget</b> | Additional funding required including MR  | <b>¥53M</b>  |

**Note:** The ¥28M–¥53M funding gap is to be closed through additional government grants, new corporate partnerships, or bridge financing secured during Phase 2 (M10–M18). The funding stack above reflects commitments and realistic pipeline as of May 2026 — it is not a target to be artificially inflated. The gap is shown explicitly because stakeholders deserve an honest picture.

---

*Derived from* `mitsue_implementation_plan.md` — May 2026
